
Armijo Reroute Project Summary

Date started December 18, 2025

Date completed March 19, 2026

Stats:

1,169 feet of new trail built (0.22 miles)


1,114 feet of old trail obliterated

Elevation at top **7,557 ft**

Elevation at bottom **7,459 ft**

-121 ft elevation loss; **+4 ft** elevation gain

maximum slope **16%**

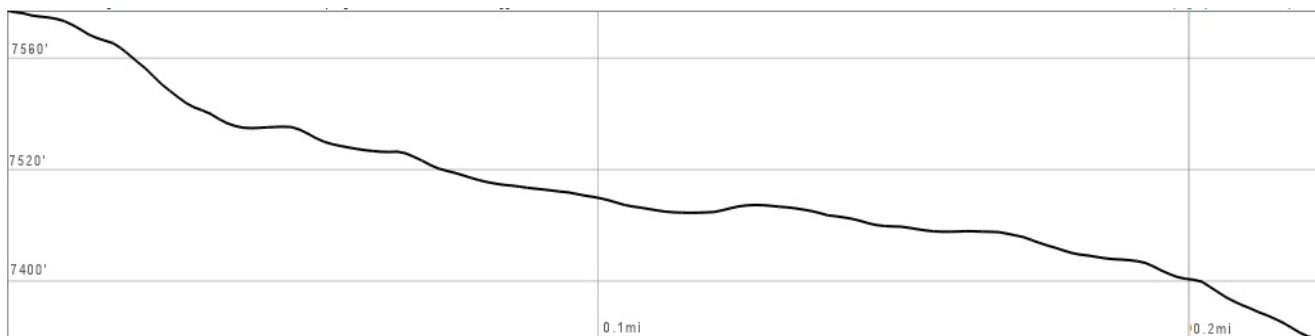

5 work days:

Day 1 12/18/2025 295 ft

Day 2 2/26/2026 178 ft

Day 3 3/5/2026 242 ft

Day 4 3/12/2026 194 ft

Day 5 3/19/2026 260 ft

TOTAL 1,169 ft

Work included:

- Reroutes out of eroded drainage.
- Cleaned out the upper junction with Faulty from water collecting.
- Cleared out fallen trees near medallion tree.
- Replaced rotted wooden signpost with metal.
- Numerous edits and finishing work.

Armijo Reroute Project

December 18, 2025 to March 19, 2026



Medallion Tree

FAULTY TRAIL

FAULTY TRAIL

Day 1
295 ft

Day 5
109 ft

Day 2
178 ft

Day 3
242 ft

Day 4
194 ft

Day 5
151 ft

ARMIJO TRAIL

ARMIJO TRAIL

- 1,169 feet of new trail built (0.22 miles)
- - - 1,114 feet of old trail obliterated
- Elevation at top 7,557 ft
- Elevation at bottom 7,459 ft
- 121 ft elevation loss; +4 ft elevation gain
- maximum slope 16%

100 ft
